

## What's Happening:

Drywall install is in full swing in the first sequence with taping and finishing following right behind. Mechanical, electrical, plumbing, and fire protection continue their rough-in, and overhead installation is taking off. The metal framing and insulation is nearly complete with only a few areas to finish out. Overhead doors were installed during the past week and all openings have been sealed up with drywall finishing ongoing in the interior. As drywall finishing progresses in the coming weeks, the painter will begin in select areas.

At the exterior, the masons have completed the trash enclosure and brick veneer, and now have started the stone veneer installation at the main entrance. Metal panel installation is ongoing around the west elevation of the building. The site concrete has wrapped up to make way for asphalt. This allowed the binder course of asphalt to be installed on portions of the project and will finish out in the coming weeks. We have seen this project move quickly as we head towards the fall and winter months with all the site and enclosure work taking place!



*The asphalt binder course was installed adjacent to the site concrete and notice the overhead door installed in the right side of the image!*



*The masons have finished installing the brick veneer and have started installing the stone veneer seen behind the scaffold.*



*Drywall installation and finishing will be moving quickly over the next few weeks to prepare spaces to receive paint.*

## DID YOU KNOW?


Asphalt pavement is the USA's most recycled product at nearly a 99% recycle rate. Even use after use, the asphaltic cement retains its value of cohesiveness no matter how many times it is recycled. Using recycled asphalt eliminates waste from our landfills and lowers paving costs!

## Questions?

Project Manager, Matt McDonald / (608)-301-6169 / [mmcdonald@findorff.com](mailto:mmcdonald@findorff.com)



Metal panel install continues overtop of the foam insulation and soon the exterior of the build will receive the metal panel trim.

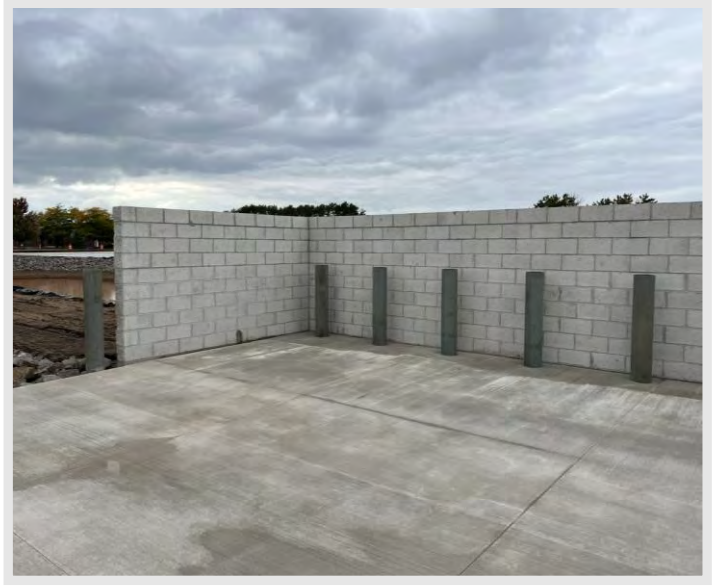

The masons have completed their install of the block trash enclosure and the concrete slab with bollards has been placed.



Overhead mechanical, electrical, plumbing, and fire protection trades have started to take off in sequence with the drywall. Notice all the different systems in the above photo – it takes a lot to bring a project to life!

## Questions?

Project Manager, Matt McDonald / (608)-301-6169 / [mmcdonald@findorff.com](mailto:mmcdonald@findorff.com)
